



Grove Park Streetscape Improvement Scheme  
Progress Report Progress Report No. 7 28/11/18 to  
12/12/18



## Grove Park Streetscape Improvement Scheme Site Overview

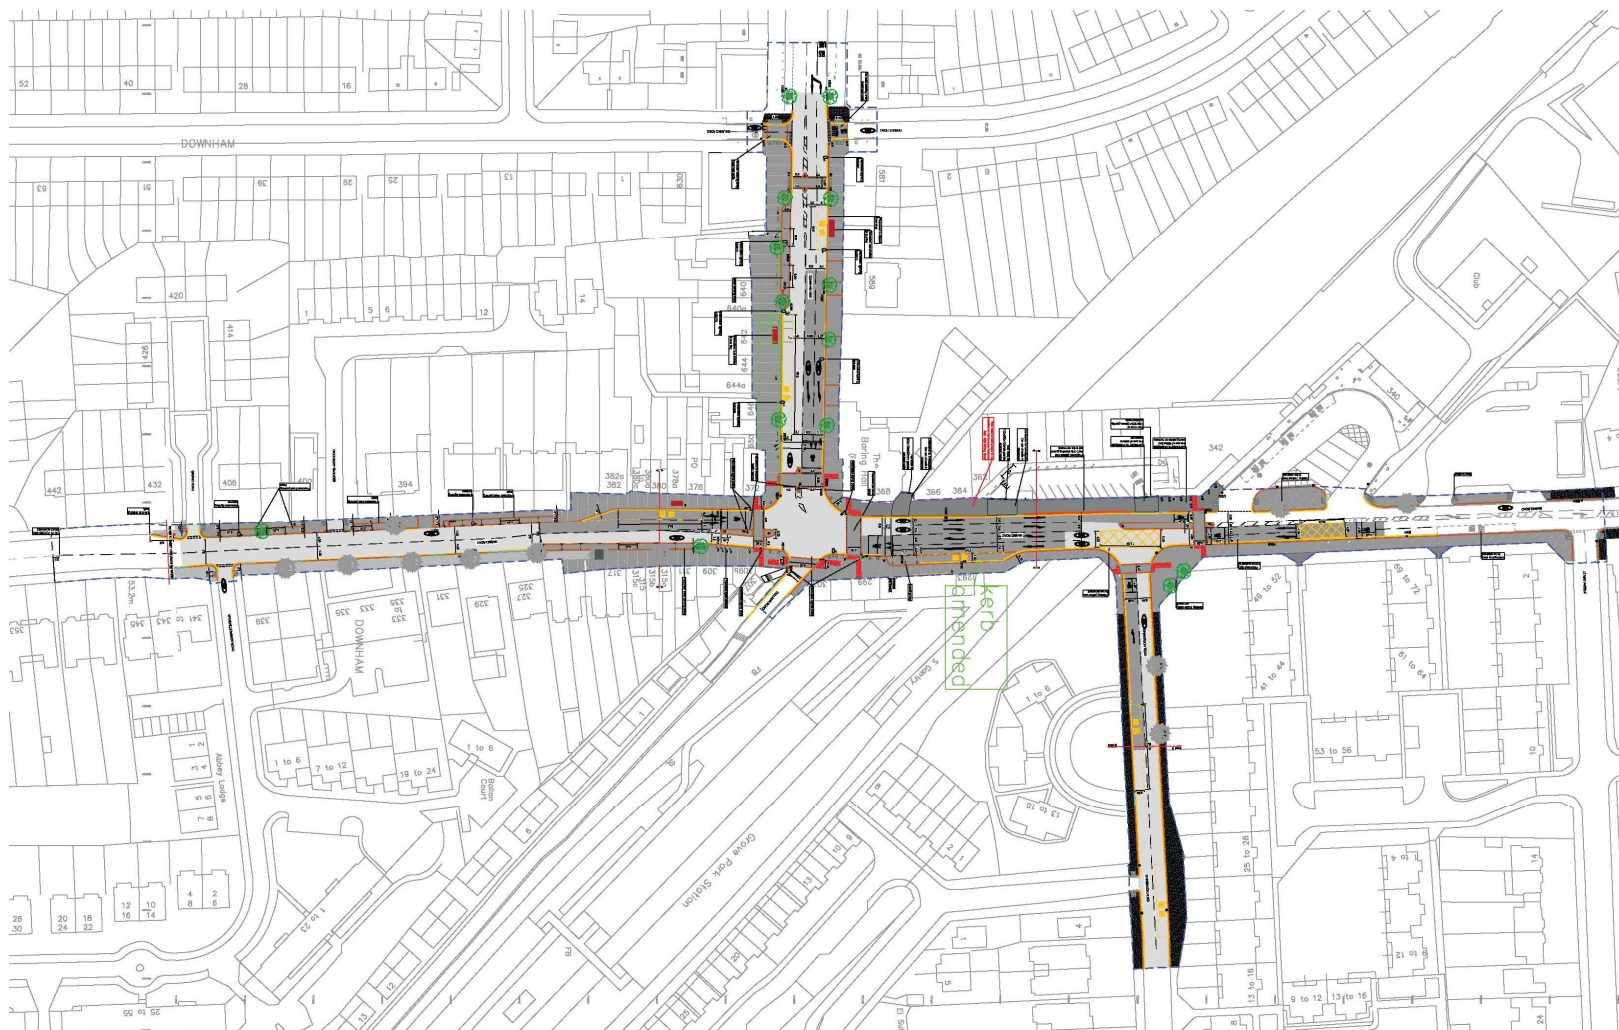

## Grove Park Streetscape Improvement Scheme Project Phasing

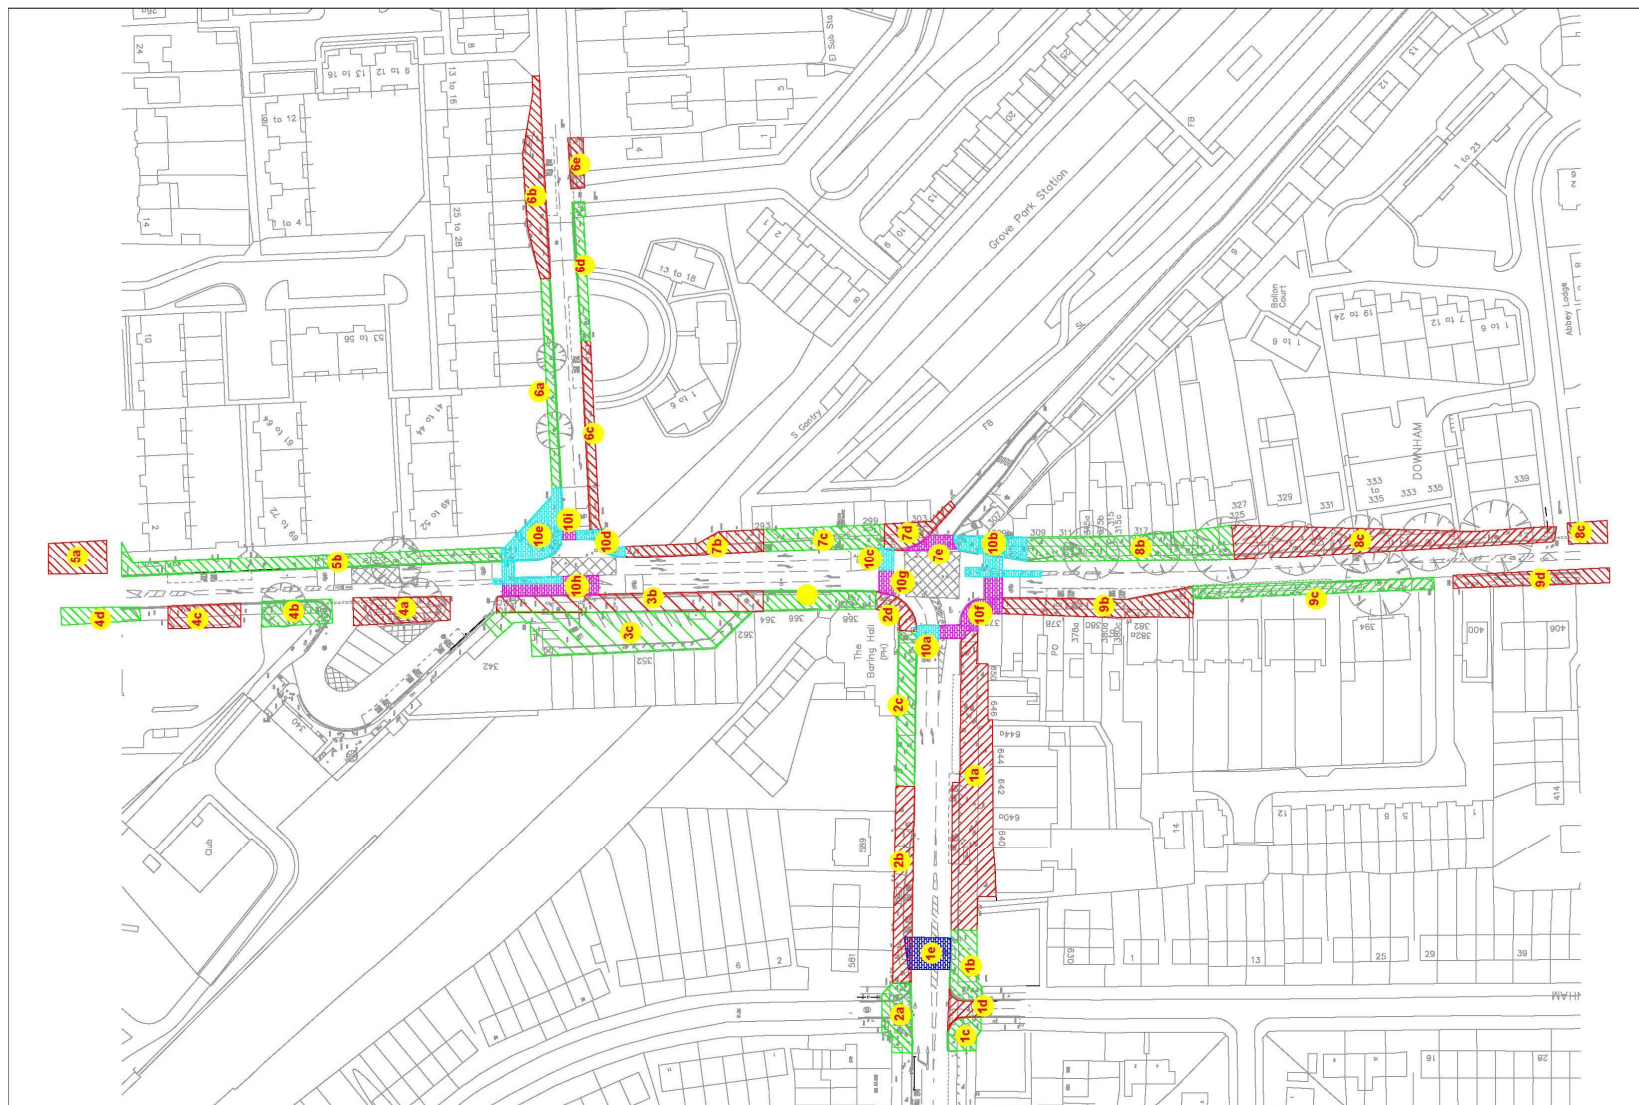

## Grove Park Streetscape Improvement Scheme Project Update

<b>Phase 1a</b>		<b>86%</b>
Site Clearance	100%	
Kerbs Installation	100%	
Paving Installation	100%	
Drainage	100%	
Street Furniture	0%	
Blocks Installation	100%	
Traffic Signals	100%	
<b>Phase 1b</b>		<b>80%</b>
Site Clearance	100%	
Kerbs Installation	100%	
Paving Installation	100%	
Blocks Installation	100%	
Street Furniture	0%	
<b>Phase 1c</b>		<b>74%</b>
Site Clearance	100%	
Kerbs Installation	100%	
Paving Installation	95%	
Street Furniture	0%	
<b>Phase 1d</b>		<b>100%</b>
Site Clearance	100%	
Kerbs Installation	100%	
Paving Installation	100%	
Drainage	100%	
Blocks Installation	100%	



<b>Phase1e</b>		<b>70%</b>
Site Clearance		70%
Kerbs Installation		70%
Blocks Installation		70%
<b>Phase 2a</b>		<b>0%</b>
Site Clearance		0%
Kerbs Installation		0%
Paving Installation		0%
Blocks Installation		0%
<b>Phase 2b</b>		<b>9%</b>
Site Clearance		30%
Kerbs Installation		15%
Paving Installation		0%
Drainage		0%
Street Furniture		0%
<b>Phase 2c</b>		<b>77%</b>
Site Clearance		80%
Kerbs Installation		100%
Paving Installation		80%
Drainage		100%
Street Furniture		0%
Traffic Signals		100%
<b>Phase 2d</b>		<b>80%</b>
Site Clearance		100%
Kerbs Installation		100%
Paving Installation		100%
Street Furniture		0%
Traffic Signals		100%



<b>Phase 3a</b>		<b>62%</b>
Site Clearance		70%
Kerbs Installation		70%
Paving Installation		70%
Street Furniture		0%
Traffic Signals		100%
<b>Phase 3b</b>		<b>46%</b>
Site Clearance		25%
Kerbs Installation		25%
Paving Installation		25%
Drainage		100%
Street Furniture		0%
Traffic Signals		100%
<b>Phase 3c</b>		<b>0%</b>
<b>Phase 4a</b>		<b>80%</b>
Site Clearance		100%
Kerbs Installation		100%
Paving Installation		100%
Drainage		100%
Street Furniture		0%
<b>Phase 4b</b>		<b>43%</b>
Site Clearance		50%
Kerbs Installation		50%
Drainage		20%
Paving Installation		50%
<b>Phase 4c</b>		<b>0%</b>
Site Clearance		0%
Kerbs Installation		0%
Paving Installation		0%



<b>Phase 4d</b>		<b>0%</b>
Site Clearance		0%
Kerbs Installation		0%
Paving Installation		0%
<b>Phase 5a</b>		<b>0%</b>
Site Clearance		0%
Kerbs Installation		0%
Paving Installation		0%
<b>Phase 5b</b>		<b>100%</b>
Site Clearance		100%
Kerbs Installation		100%
Paving Installation		100%
Drainage		100%
Traffic Signals		100%
<b>Phase 6a</b>		<b>0%</b>
Site Clearance		0%
Kerbs Installation		0%
Paving Installation		0%
<b>Phase 6b</b>		<b>0%</b>
Site Clearance		0%
Kerbs Installation		0%
Paving Installation		0%
<b>Phase 6c</b>		<b>0%</b>
Site Clearance		0%
Kerbs Installation		0%
Paving Installation		0%
<b>Phase 6d</b>		<b>0%</b>
Site Clearance		0%
Kerbs Installation		0%
Paving Installation		0%



<b>Phase 6e</b>		<b>0%</b>
Site Clearance		0%
Kerbs Installation		0%
Paving Installation		0%
<b>Phase 7b</b>		<b>100%</b>
Site Clearance		100%
Kerbs Installation		100%
Paving Installation		100%
Drainage		100%
Blocks Installation		100%
<b>Phase 7c</b>		<b>100%</b>
Site Clearance		100%
Kerbs Installation		100%
Paving Installation		100%
Drainage		100%
Blocks Installation		100%
<b>Phase 7d</b>		<b>100%</b>
Site Clearance		100%
Kerbs Installation		100%
Paving Installation		100%
Traffic Signals		100%



<b>Phase 7e</b>		<b>100%</b>
Site Clearance		100%
Kerbs Installation		100%
Blocks Installation		100%
<b>Phase 8b</b>		<b>0%</b>
Site Clearance		0%
Kerbs Installation		0%
Paving Installation		0%
<b>Phase 8c</b>		<b>0%</b>
Site Clearance		0%
Kerbs Installation		0%
Paving Installation		0%
<b>Phase 9b</b>		<b>100%</b>
Site Clearance		100%
Kerbs Installation		100%
Paving Installation		100%
<b>Phase 9c</b>		<b>57%</b>
Site Clearance		50%
Kerbs Installation		70%
Paving Installation		50%
Blocks Installation		40%
<b>Phase 9d</b>		<b>36%</b>
Site Clearance		50%
Kerbs Installation		70%
Blocks Installation		0%
Paving Installation		25%



<b>Phase 10a</b>		<b>100%</b>
Site Clearance		100%
Kerbs Installation		100%
Blocks Installation		100%
<b>Phase 10b</b>		<b>83%</b>
Site Clearance		100%
Kerbs Installation		100%
Blocks Installation		100%
Drainage		100%
Traffic Signals		100%
Street Furniture/Traffic Signs		0%
<b>Phase 10c</b>		<b>100%</b>
Site Clearance		100%
Kerbs Installation		100%
Blocks Installation		100%
<b>Phase 10d</b>		<b>100%</b>
Site Clearance		100%
Kerbs Installation		100%
Blocks Installation		100%
Kerbs Installation		100%
Paving Installation		100%
<b>Phase 10e</b>		<b>100%</b>
Site Clearance		100%
Kerbs Installation		100%
Blocks Installation		100%



<b>Phase 10f</b>		<b>88%</b>
Site Clearance	100%	
Kerbs Installation	100%	
Blocks Installation	100%	
Kerbs Installation	100%	
Paving Installation	100%	
Drainage	100%	
Traffic Signals	100%	
Street Furniture/Traffic Signs	0%	
<b>Phase 10g</b>		<b>100%</b>
Site Clearance	100%	
Kerbs Installation	100%	
Blocks Installation	100%	
<b>Phase 10h</b>		<b>100%</b>
Site Clearance	100%	
Kerbs Installation	100%	
Blocks Installation	100%	



Grove Park Streetscape Improvement Scheme  
Programme

▲ GROVE PARK SCHEME	169 days	Thu 19/07/18	Thu 28/02/19
▲ Phase 1- s/w crossing on Downham Way to junction of Galahad Rd	40 days	Mon 08/10/18	Tue 27/11/18
▲ Phase 2 - The junction of Reigate Rd/Downham Way to n/w crossing on Downham way	37 days	Wed 03/10/18	<u>Mon 19/11/18</u>
▲ Phase 3- the junc of Downham Way /Baring Rd to entrance to bus station	81 days	Fri 05/10/18	Tue 22/01/19
▲ Phase 4 - bus station entrance to north end of works (areas 4a-d)	29 days	Mon 22/10/18	Tue 27/11/18
▲ Phase 5- Le May Ave /Baring Rd (area 5a)	6 days	Tue 20/11/18	Tue 27/11/18
▲ Phase 6- Chinbrook Road (north and south footways)	44 days	Wed 28/11/18	<u>Mon 28/01/19</u>
▲ Phase 7	64 days	Mon 03/09/18	Mon 19/11/18
▲ Phase 8 - the junc of Pullman Mews /Baring Rd to woodville manor Rd	59 days	Wed 03/10/18	<u>Wed 19/12/18</u>
▲ Phase 9 - Downham Way/Baring Rd to 432, Baring Rd	46 days	Tue 09/10/18	Thu 06/12/18
▲ Phase 10 -sections a to e	58 days	Thu 19/07/18	<u>Mon 01/10/18</u>
▲ Phase 10 -sections f to i	56 days	Fri 10/08/18	Thu 18/10/18
▲ Phase 11- carriageway resurfacing	9 days	Mon 18/02/19	Thu 28/02/19
Phase 12- Street furniture installations	10 days	Mon 10/12/18	Fri 21/12/18
Phase 13- Tree pit paving	12 days	Thu 24/01/19	Fri 08/02/19
Commissioning of Signals (Provisional)			Wed 02/01/19
